

Gray Elementary

Opening August 2023

Face Brick and Stone Progress

Interior Framing is On-Going

Roof Progress



James E. Steenbergen Middle School

Opening August 2024

Construction Contract A101 Executed

Contractor Working on Providing Bonds & Insurance




Viola Randle Elementary School (33)

Opening August 2024

Construction Documents issued for Proposals

Construction Manager at Risk Subcontractor Proposals Due November 17

Guaranteed Maximum Price (GMP) #1
Recommendation on December Board Agenda

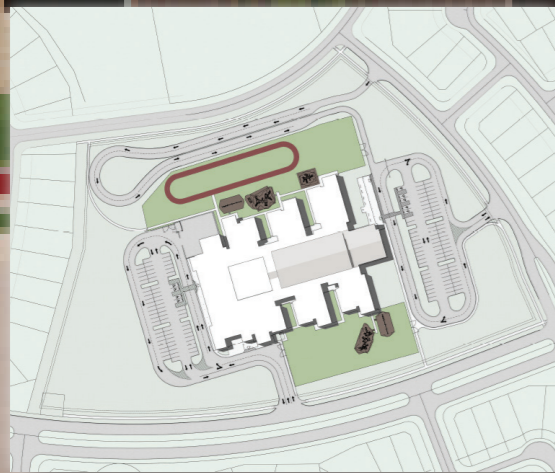

Willie Melton Sr. Elementary School (34)

Opening August 2024

Construction Documents issued for Proposals





Proposal Opening November 15



Contractor Recommendation on
December Board Agenda

WILLIE MELTON SR. ELEMENT

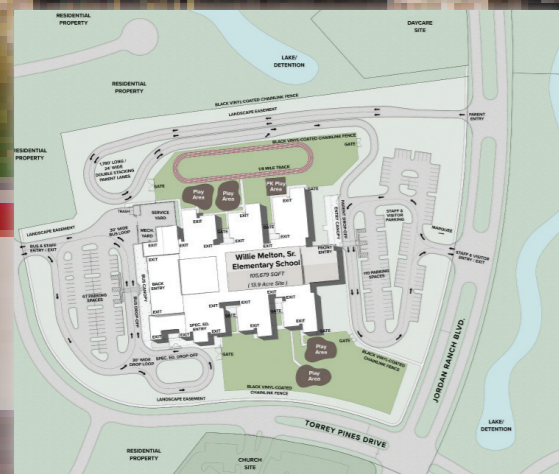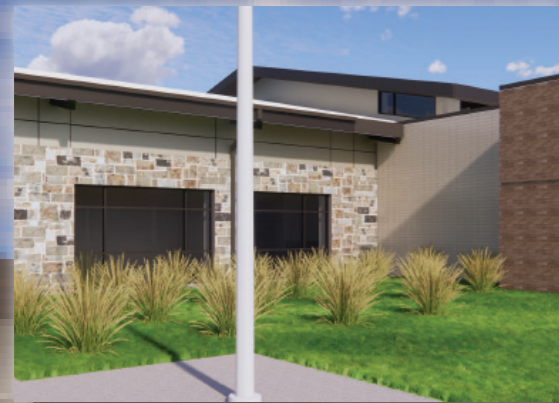

Austin Elementary Additions & Renovations

Complete April 2023

Front Vestibule Sidewalk Poured

Vestibule Sheetrock Installation Progress

Lightfixture Installation



Beasley Elementary Additions & Renovations

Complete February 2023

Aluminum Storefront Progress

Mechanical Roof Curb Installed

Roof Progress



Bowie Elementary Additions & Renovations

Complete January 2023

Unit Ventilators Installed North Wing
Classrooms

New Admin Space Paint Progress

Staff Restrooms Progress



Campbell Elementary Re-Roof

Complete November 2022

Project Is Close to Substantial Completion



Dickinson Elementary Re-Roof

Complete December 2022

Installation of Standing Roof On-Going

Standing Roof Material Progress

Finalizing Brick Thru-Wall Installation




George Junior High Renovations

Complete January 2024

Phase II - GMP 3 Scheduled for December Board Approval

First Floor New Casework Schedule for Summer of 2023

Membrane and Base Ply Progress

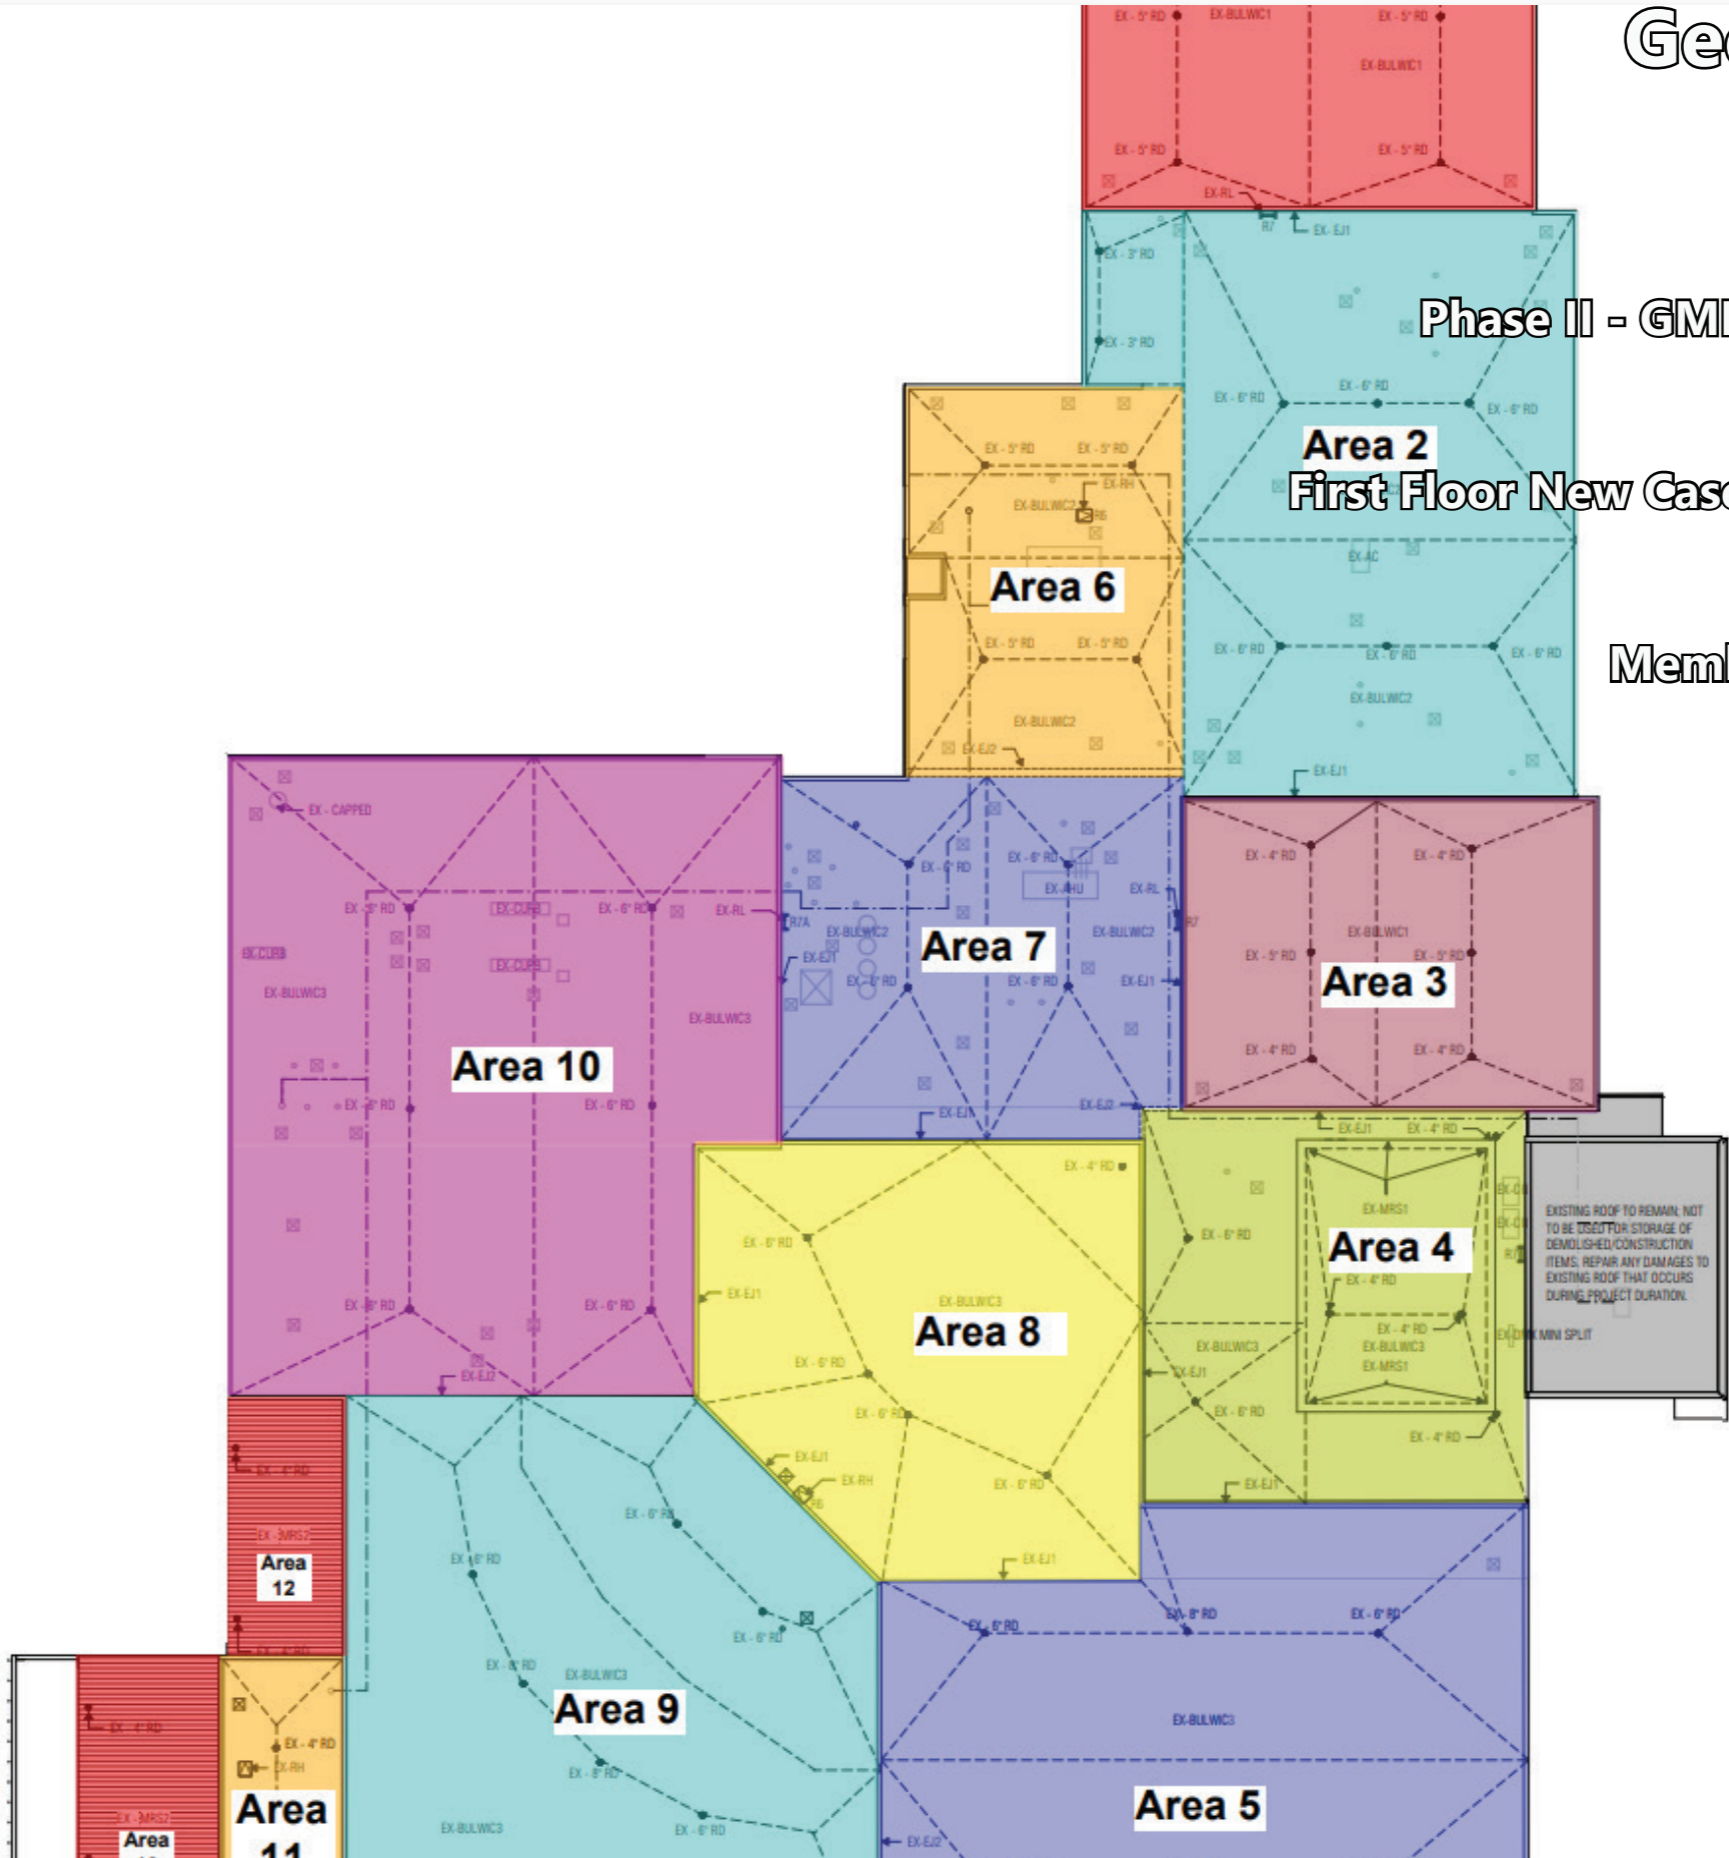


Huggins Elementary Additions & Renovations

Complete January 2023

Exterior Stucco Plaster Wall Finish Complete

Addition Interior Finishes Are Installed

Re-Roof Complete

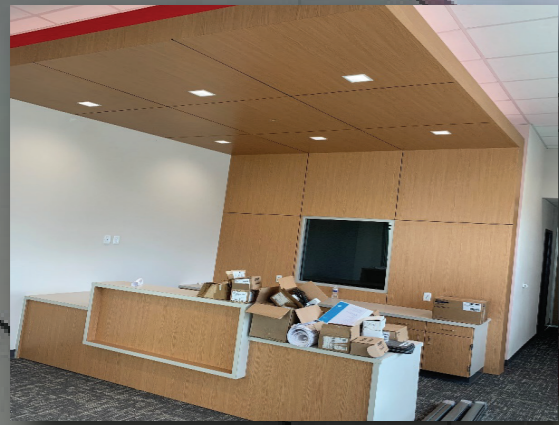

Jackson Elementary Additions & Renovations

Complete December 2022

Service Drive Progress

Clinic Bathroom Complete

New Roof Access



Lamar Consolidated High School New Tennis Courts

Complete October 2022

Tennis Court Project Substantially Complete

Punch List Correction On-Going

Close-Out Documents In Process of Being Reviewed

