


Facilities Assessment & Long Range Facilities Plan

- Facilities & Planning has been working with PBK Architects, Inc.
- Kick off meeting was held 3/22.
- Questionnaire will be distributed to Principals, Directors, etc. on 4/19.



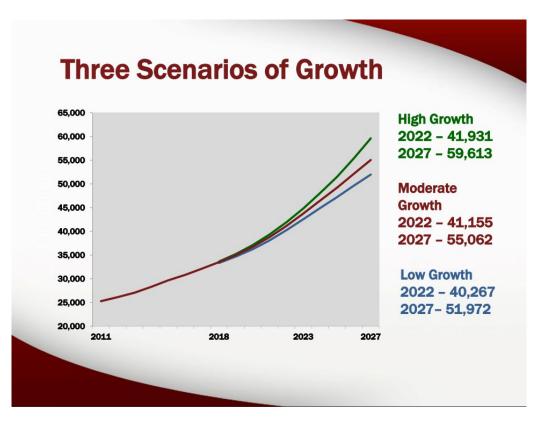


Austin Elementary & Seguin ECC Roof Replacement

• Austin Elementary

• Complete

Seguin Early Childhood Center

- Project is complete
- Project is scheduled for close out in May 2019

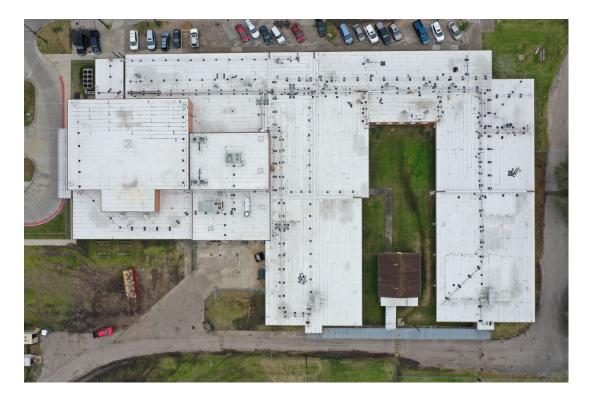



Classroom Intruder Lockset Project

- Electrified hardware (door buzzers) have been installed.
- Classroom Security Intruder Original Scope of work complete. Punch list is on-going. All items to be complete in four weeks.






Child Nutrition Serving Lines

• Terry HS new cafeteria serving lines:

- Additional serving line upgrade recommendation is on this Board agenda. Construction scheduled for this summer 2019.
- George JH new cafeteria serving lines:
 - Additional serving line upgrade recommendation is on this Board agenda. Construction scheduled for this summer 2019.



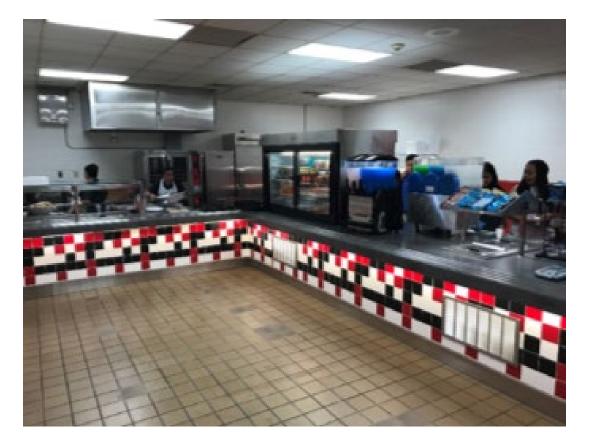

High School #6 & Junior High School #6

- The Guaranteed Maximum Price (GMP) recommendation has been established and on this Board Agenda.
- Offsite drainage and offsite utilities will be included in a future amendment.
- Fort Bend County MUD #162 Annexation



3D ENTRANCE PERSPECTIVE NEW LAMAR CONSOLIDATED HIGH SCHOOL 6 - OPTION 1





Synthetic Turf & Track Project

- Synthetic turf replacement at Foster, Fulshear, George Ranch, and Terry High Schools.
- Track replacement at Foster.
- Foster, Terry, and Fulshear construction has begun.
- George Ranch will commence after regional and state track meets.





Synthetic Turf & Track Images as of 4/10

Foster High School

Terry High School





Foster High School Athletic Improvements

- This project includes improvements to the Baseball/Softball dugouts, backstops and the replacement of lockers in the fieldhouse.
- Preconstruction meeting was held with Millis on 4/2.
- Lockers will be installed by August 1.





• Lamar Consolidated Complex Athletic & Site Improvements

- PBK Sports is the Architect of Record.
- This project will include:
 - New Sub-varsity stadium
 - Revise the parent pickup/drop-off at Lamar Junior High
 - Improve the drainage, drives, and sidewalks for safety
- A Design Kick off meeting was held and initial schemes are being developed.

• Traylor Stadium Press box Replacement


• A Design Kick off meeting was held and initial schemes are being developed.



Multi-Campus Improvements

- Williams ES Carpet Replacement, Fire Sprinkler System and Administration Office Renovations.
- Campbell ES Carpet and Vinyl wall covering Replacement.
- Navarro MS Carpet Replacement & New Intercom System.
- Wessendorff Carpet and Vinyl wall covering Replacement.
- Contractor recommendation is on this Board Agenda.



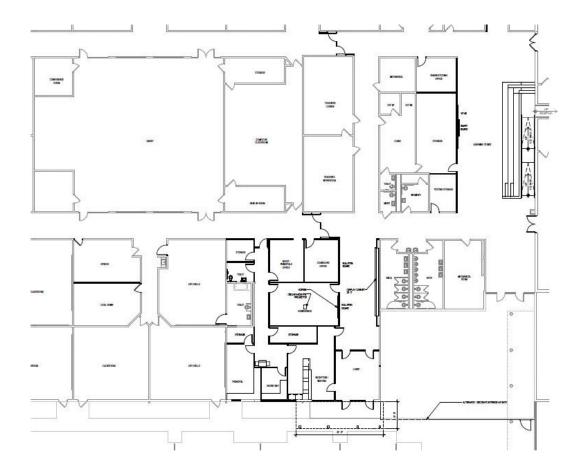

ALC Addition and Renovations

- VLK Architects is the Architect of Record.
- Kick off meeting was held 3/28.

• Jane Long Historical Gym Renovations

- VLK Architects is the Architect of Record.
- Kick off meeting scheduled for 4/17.

• LOTE Lab Equipment Project

• Vendor proposal recommendation is scheduled to be on the May Board Agenda.



Freezer/Cooler Replacements

- Competitive Sealed Proposals were opened 4/2.
- Contractor recommendation is scheduled on this Board Agenda.





Transportation Fuel Tank Replacement



Bond 2017 LAMAR CONSOLIDATED ISD Morris & Associates are starting the design of a new fuel island and new above ground storage tanks.

Bond 2017 April Board Agenda Items

- Consider approval of guaranteed maximum price amendment to the contract with Drymalla Construction Company
- Consider approval of CSP#13-2019RG for multi-campus renovations at Campbell Elementary, Navarro Middle, Wessendorff Middle, and Williams Elementary Schools
- Consider approval of moving services for the multi-campus renovations at Campbell Elementary, Navarro Middle, Wessendorff Middle, and Williams Elementary Schools
- Consider approval of serving line renovations at Terry High School
- Consider approval of serving line renovations at George Junior High School
- Consider approval of CSP#10-2019LN for the cooler/freezer replacements
- Consider approval of Fort Bend County MUD #162 additional annexation fees.



2017 BOND REFERENDUM SUMMARY			
PROJECT NAME	PROJECT BUDGET	COMMITTED	BALANCE
114 Austin ES Re-Roof	\$1,900,000.00	\$850,472.00	\$1,049,528.00
117 Seguin ECC Re-Roof	\$1,900,000.00	\$926,994.00	\$973,006.00
002 Terry HS Serving Lines	\$650,000.00	\$203,636.32	\$446,363.68
042 George JHS Serving Lines	\$650,000.00	\$207,480.40	\$442,519.60
Classroom Intruder Locks	\$400,000.00	\$390,985.72	\$9,014.28
011 High School #6	\$126,500,000.00	\$3,362,515.00	\$123,137,485.00
046 Junior High School #6	\$62,000,000.00	\$1,678,435.00	\$60,321,565.00
Lamar CHS Adds & Renov.	\$13,640,000.00	\$0.00	\$13,640,000.00
New Elementary School #29 (146)	\$30,200,000.00	\$0.00	\$30,200,000.00
High School LOTE Lab Renovations	\$1,050,000.00	\$47,250.00	\$1,002,750.00
HS Field Turf Replace & Foster HS Track	\$9,250,000.00	\$895,300.00	\$8,354,700.00
Foster HS Athletic Improvments	\$700,000.00	\$32,950.00	\$667,050.00
Camp. ES, Will. ES, Nav. MS & Wess. MS Improv.	\$2,740,000.00	\$126,575.00	\$2,613,425.00
Jane Long ES Historical Gym Renovations (105)	\$3,325,000.00	\$144,000.00	\$3,181,000.00
ES Cooler/Freezer Replacement	\$1,400,000.00	\$63,000.00	\$1,337,000.00
Transportation - Replace Underground Fuel Tank	\$900,000.00	\$40,500.00	\$859 <i>,</i> 500.00
New Alternative Learning Center	\$12,200,000.00	\$33,750.00	\$12,166,250.00

2017 BOND TECHNOLOGY SUMMARY										
PROJECT NAME	PROJECT BUDGET	COMMITTED	BALANCE							
+	\$9,044,000.00	\$2,648,747.79	\$6,395,252.21							
PTO-Printer Refresh	\$1,440,000.00	\$448,046.34	\$991,953.66							
CCU-Campus Core Uplink	\$740,000.00	\$518,915.05	\$221,084.95							
ESO-Expanded Storage	\$400,000.00	\$400,000.00	\$0.00							
SCO-Security Cameras	\$250,000.00	\$250,000.00	\$0.00							
TEL-Telephones	\$890,000.00	\$50,000.00	\$840,000.00							
TOTAL TECHNOLOGY BOND	\$34,326,000.00									
REMAINING TECHNOLOGY BOND	\$30,010,290.82									

2017 BOND TRANSPORTATION SUMMARY										
PROJECT NAME	PROJECT BUDGET	COMMITTED	BALANCE							
New Bus Purchase	\$2,568,046.00	\$2,568,046.00	\$0.00							
Smart Tag	\$500,000.00	\$0.00								



1st SALE	2018		2019		2020		2021		2022			2023
PROJECTS	SEPT OCT NOV	JAN JAN FEB MAR MAV	JUNE JULY AUG SEPT OCT	NOV DEC JAN FEB MAR MAY	JUNE JULY ALIG	SEPT OCT OCT DEC JAN FEB MAR	APK MAY JUNE JULY AUG SEPT	DEC DEC JAN	MAR APR MAY JUNE JULY AUG	SEPT OCT NOV DEC	JAN FEB MAR APR MAY	JUNE JULY AUG SEPT SEPT OCT NOV DEC
Austin ES & Seguin ES Re-Roof	CONST	WARRANTY										
Terry HS & George JHS Serving Lines	CONSTRU	ICTION	WARF	RANTY								
Classroom Intruder Locksets	CONSTRU		RANTY									
High School 6 & Junior High 6	D C	D P	CONSTRUCTIO	N			WARRANTY					
High School Artificial Turf & Tracks	I	D CD P CON	ST WARF	RANTY								
Foster HS Athletic Improvements	I	D CD P CON	ST WARF	ANTY								
CES, WES, WMS, NMS Improv.	I	D CD P CON	ST WARF	RANTY								
ES Cooler/Freezer Replacement	I	D <mark>CD P</mark> C		ANTY								
Fuel Tank Replacement		D CD P	CONST	WARRANTY								
Lamar Complex Exterior Improvements	I	DESIGN CD	P CO	NSTRUCTION		WARRAN	тү					
Traylor Stadium Pressbox		DESIGN	CD	P CONSTRUCTION		WARRANTY						
High School LOTE Lab Installation		D P C		ITY								
Jane Long Historical Gym Renovations		DESIGN	CD	P CONSTRUCTION		WARRANTY						
Elementary (#29)		Ľ	CD	P CONSTRUCTION		L L	VARRANTY					
		JAN JAN FEB MAR APR		NOV JAN FEB MAR MAY	JUNE	SEPT OCT DEC JAN FEB MAR	MAY JUNE JULY AUG SEPT	DEC DEC JAN	MAR APR MAY JUNE JULY AUG	SEPT OCT NOV DEC	JAN FEB MAR APR MAY	JUNE JULY AUG SEPT OCT NOV DEC
	2018		2019		2020		2021		2022			2023

LAMAR CISD 2017 BOND PROGRAM - PROJECT LIST



2nd SALE	2018		2019				2020			2021			2022			2023	
PROJECTS	SEPT OCT NOV DEC	JAN FEB MAR APR MAY	JUNE JULY AUG	SEPT OCT NOV	DEC	FEB Mar Apr May	JULY	SEPT SEPT OCT NOV	JAN FEB MAR APR	JUNE	SEPT SEPT OCT NOV DEC	JAN FEB MAR APR	JUNE JULY AUG	SEPT OCT NOV	JAN FEB MAR		SEPT OCT NOV
ALC Additions & Renovations		DESIGN	CD	Р	CONS	TRUCTION			WARRANTY								
Lamar HS & JHS Add & Renov.*				DESIG	N	CD	Р	ONSTRUCTI	ON		WARRANT	Y					
Terry HS & GJHS Add & Renov.*				DESIG	N	CD	P C	ONSTRUCTI	ON		WARRANT	Y					
Austin, Bowie & Jackson mprov.*				D C	1 D	P CONST		WARRANT	γ								
FHS, BJHS, JES, PES, LES mprov.*				D C	D 1	P CONST		WARRANT	Y								
Exterior Improv. SES, TRES, FHS*				D C	D I	P CONST		WARRANT	Y								
Seimans Controls Upgrade*				d C	D 1	P CONST		WARRANT	Ŷ								
HS Multi-Purpose*					ESIGN	CD		P CONST	RUCTION	w	ARRANTY						
Brazos Crossing Exterior*					ESIGN	CD		P CONST	RUCTION	W	ARRANTY						
MS Orchestra Additons*				Ľ	DESIGN	CD		P CONST	RUCTION	M	ARRANTY						
New Elementary 30 & 31*							D	CD	P CONSTRU	ICTION			WARRA	ΝΤΥ			
	SEPT OCT NOV DEC	JAN FEB MAR APR MAY	JULY AUG	SEPT OCT	DEC	FEB MAR MAY		SEPT SEPT OCT NOV	JAN FEB MAR APR	JUNE	SEPT OCT NOV DEC	JAN FEB MAR APR	JUNE	SEPT OCT NOV	JAN FEB MAR		SEPT OCT NOV
	2018		2019	u			2020			2021			2022			2023	

