



Bond

2017

LAMAR CONSOLIDATED ISD

Synthetic Turf & Track Project

- All projects are complete.
- Foster – Striping of the track was completed this week.
- Fields are in use.
- Final payment is scheduled for the October Board Meeting

Terry High School



Foster High School Athletic Improvements

- Lockers are complete and Football lockers are in use.
- Baseball/Softball fields are scheduled to be complete in November 2019.



Multi-Campus Improvements


- Huckabee is the Architect of Record
- This project includes:

Williams ES – Construction is complete with the exception of the Administration area. This is scheduled to be complete on August 19th.

Campbell ES- Construction is complete with the exception of a few Vinyl Wall Covering areas. These areas have been painted until the VWC is received.

Navarro MS – Construction is complete.

Wessendorff MS – Construction is complete with the exception of a few Vinyl Wall Covering areas. These areas have been painted until the VWC is received.

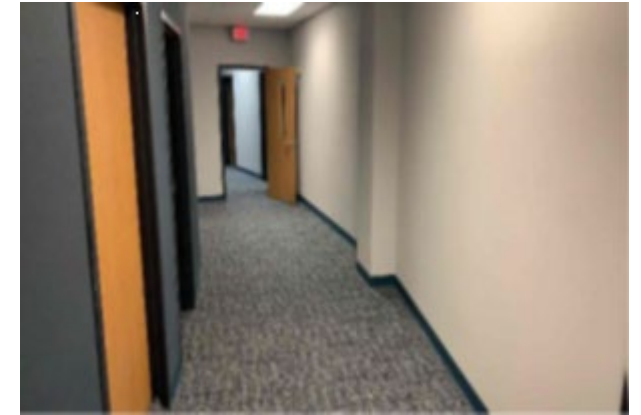

Freezer/Cooler Replacements

- Project is Complete.



ALC Addition and Renovations

- VLK Architects is the Architect of Record.
- Schematic Design is on the August Board Agenda.



Jane Long Historical Gym Renovations

- VLK Architects is the Architect of Record.
- Schematic Design is on the August Board Agenda.



LOTE Lab Equipment Project

- Installation of the LOTE Labs is complete.




Transportation Fuel Tank Replacement

- Morris & Associates is the A/E Firm of Record.
- Survey and material testing is complete.
- Design is in process.




Facilities Assessment & Long Range Facilities Plan

- Questionnaire process is complete.
- Campus site visits are wrapping up.
- Review of the information collected will begin in September.

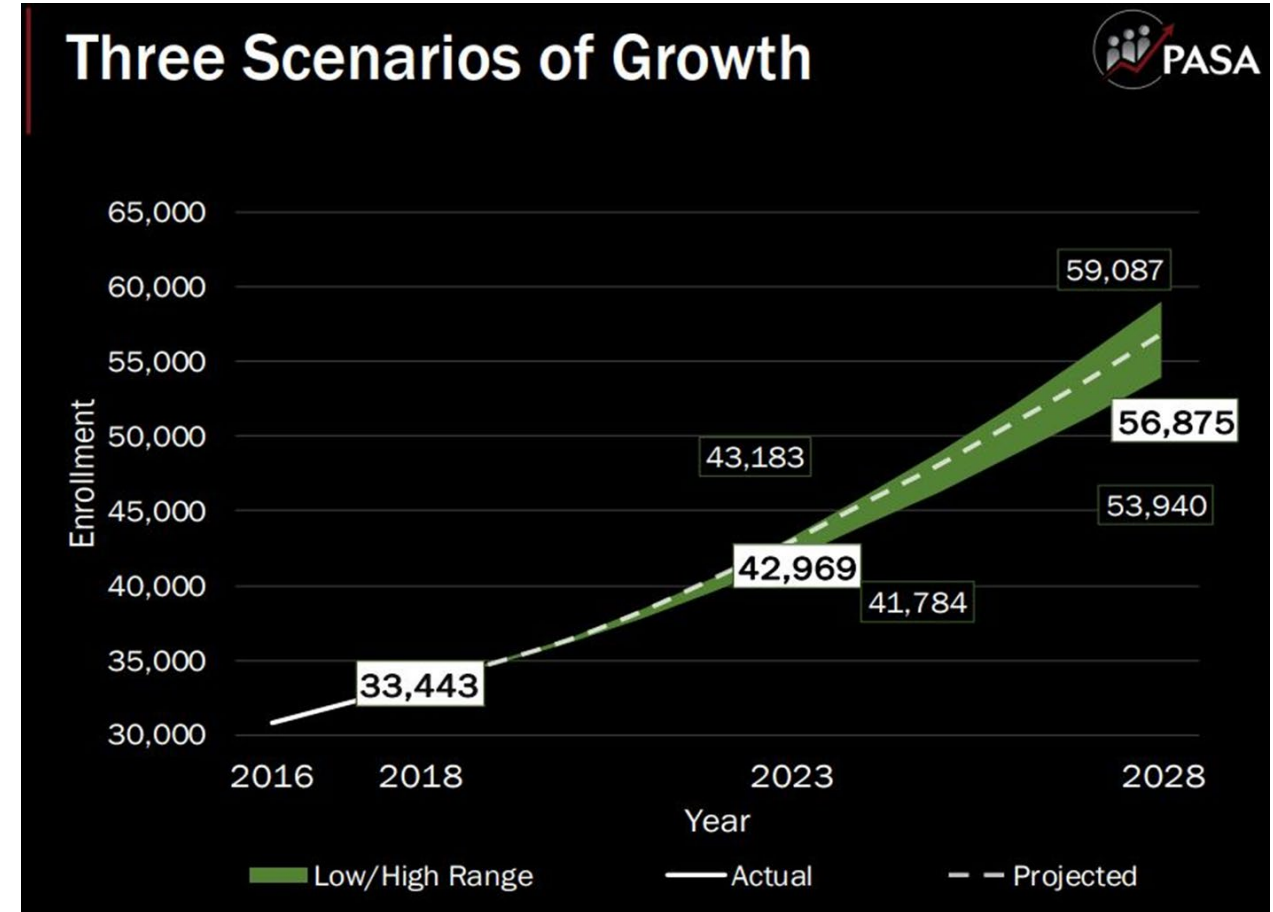

Classroom Intruder Lockset Project

- Project is complete.
- Final payment is on the August Board Agenda.

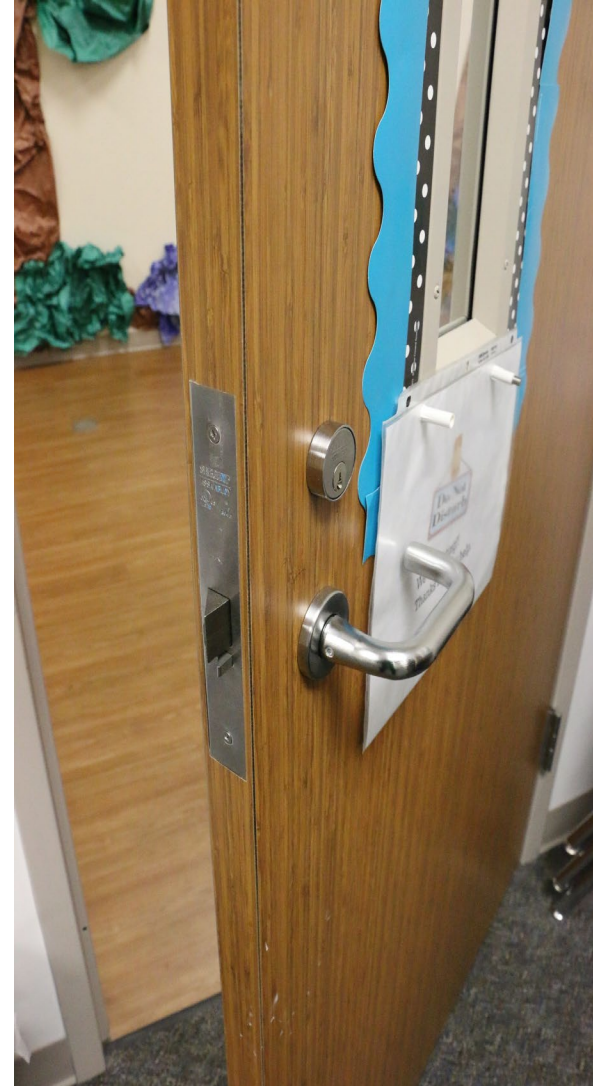

Child Nutrition Serving Lines

- **Terry HS:**
 - Installation of three new lines has started. Estimated Substantial Completion is August 19, 2019.
- **George JHS:**
 - Installation of two new lines has started. Estimated Substantial Completion is August 19, 2019.



Dr. Thomas E. Randle High School & Harry Wright Junior High School

- Construction is in progress.
- Project is on schedule.



Traylor Stadium Press Box Replacement

- Project is in the Construction Document phase.
- Contractor recommendation will be on the November Board Agenda.
- Project is scheduled to be complete in August 2020.



Bond 2017 August Board Agenda Items


- CONSIDER APPROVAL OF ARCHITECT CONTRACT FOR THE LAMAR CONSOLIDATED HIGH SCHOOL & LAMAR JUNIOR HIGH SCHOOL ADDITIONS AND RENOVATIONS
- CONSIDER APPROVAL OF ARCHITECT CONTRACT FOR THE TERRY HIGH SCHOOL AND GEORGE JUNIOR HIGH SCHOOL ADDITIONS AND RENOVATIONS
- CONSIDER APPROVAL OF SCHEMATIC DESIGN FOR THE JANE LONG HISTORIC GYM RENOVATIONS
- CONSIDER APPROVAL OF SCHEMATIC DESIGN FOR THE ALTERNATIVE LEARNING CENTER ADDITIONS AND RENOVATIONS
- CONSIDER APPROVAL OF FINAL PAYMENT FOR THE INTRUDER LOCK PROJECT

2017 BOND REFERENDUM SUMMARY			
PROJECT NAME	PROJECT BUDGET	COMMITTED	BALANCE
114 Austin ES Re-Roof	\$1,900,000.00	\$850,472.00	\$1,049,528.00
117 Seguin ECC Re-Roof	\$1,900,000.00	\$982,961.00	\$917,039.00
002 Terry HS Serving Lines	\$650,000.00	\$656,123.95	\$23,876.05
042 George JHS Serving Lines	\$650,000.00	\$528,728.39	\$91,271.61
Classroom Intruder Locks	\$400,000.00	\$390,985.72	\$9,014.28
011 Dr. Thomas E. Randle High School	\$126,500,000.00	\$110,889,146.60	\$15,610,853.40
046 Harry Wright Junior High School	\$62,000,000.00	\$52,470,415.40	\$9,529,584.60
Lamar Complex Improvements	\$10,840,000.00	\$551,124.00	\$10,288,876.00
New Elementary School #29 (146)	\$30,200,000.00	\$0.00	\$30,200,000.00
Traylor Stadium Press Box	\$2,800,000.00	\$155,216.00	\$2,644,784.00
High School LOTE Lab Renovations	\$1,050,000.00	\$198,565.00	\$851,435.00
HS Field Turf Replace & Foster HS Track	\$9,082,719.00	\$4,683,381.00	\$4,399,338.00
Foster HS Athletic Improvments	\$867,281.00	\$783,211.00	\$84,070.00
Camp. ES, Will. ES, Nav. MS & Wess. MS Improv.	\$2,854,000.50	\$2,779,302.00	\$74,698.50
Jane Long ES Historical Gym Renovations (105)	\$3,325,000.00	\$144,000.00	\$3,181,000.00
ES Cooler/Freezer Replacement	\$1,400,000.00	\$1,230,756.00	\$169,244.00
Transportation - Replace Underground Fuel Tank	\$900,000.00	\$40,500.00	\$859,500.00
New Alternative Learning Center	\$12,200,000.00	\$33,750.00	\$12,166,250.00

2017 BOND TECHNOLOGY SUMMARY			
PROJECT NAME	PROJECT BUDGET	COMMITTED	BALANCE
IFP-Interactive Flat Panel	\$9,044,000.00	\$4,030,864.71	\$5,013,135.29
PTO-Printer Refresh	\$1,440,000.00	\$1,294,954.90	\$145,045.10
CCU-Campus Core Uplink	\$740,000.00	\$518,915.05	\$221,084.95
ES0-Expanded Storage	\$400,000.00	\$400,000.00	\$0.00
SC0-Security Cameras	\$250,000.00	\$250,000.00	\$0.00
TEL-Telephones	\$890,000.00	\$50,000.00	\$840,000.00
CRO-Computer Refresh	\$20,234,000.00	\$5,600,461.30	\$14,633,538.70
TOTAL TECHNOLOGY BOND	\$34,326,000.00		
REMAINING TECHNOLOGY BOND	\$22,180,804.04		

2017 BOND TRANSPORTATION SUMMARY			
PROJECT NAME	PROJECT BUDGET	COMMITTED	BALANCE
New Bus Purchase	\$2,568,046.00	\$2,568,046.00	\$0.00
Smart Tag	\$500,000.00	\$0.00	\$500,000.00



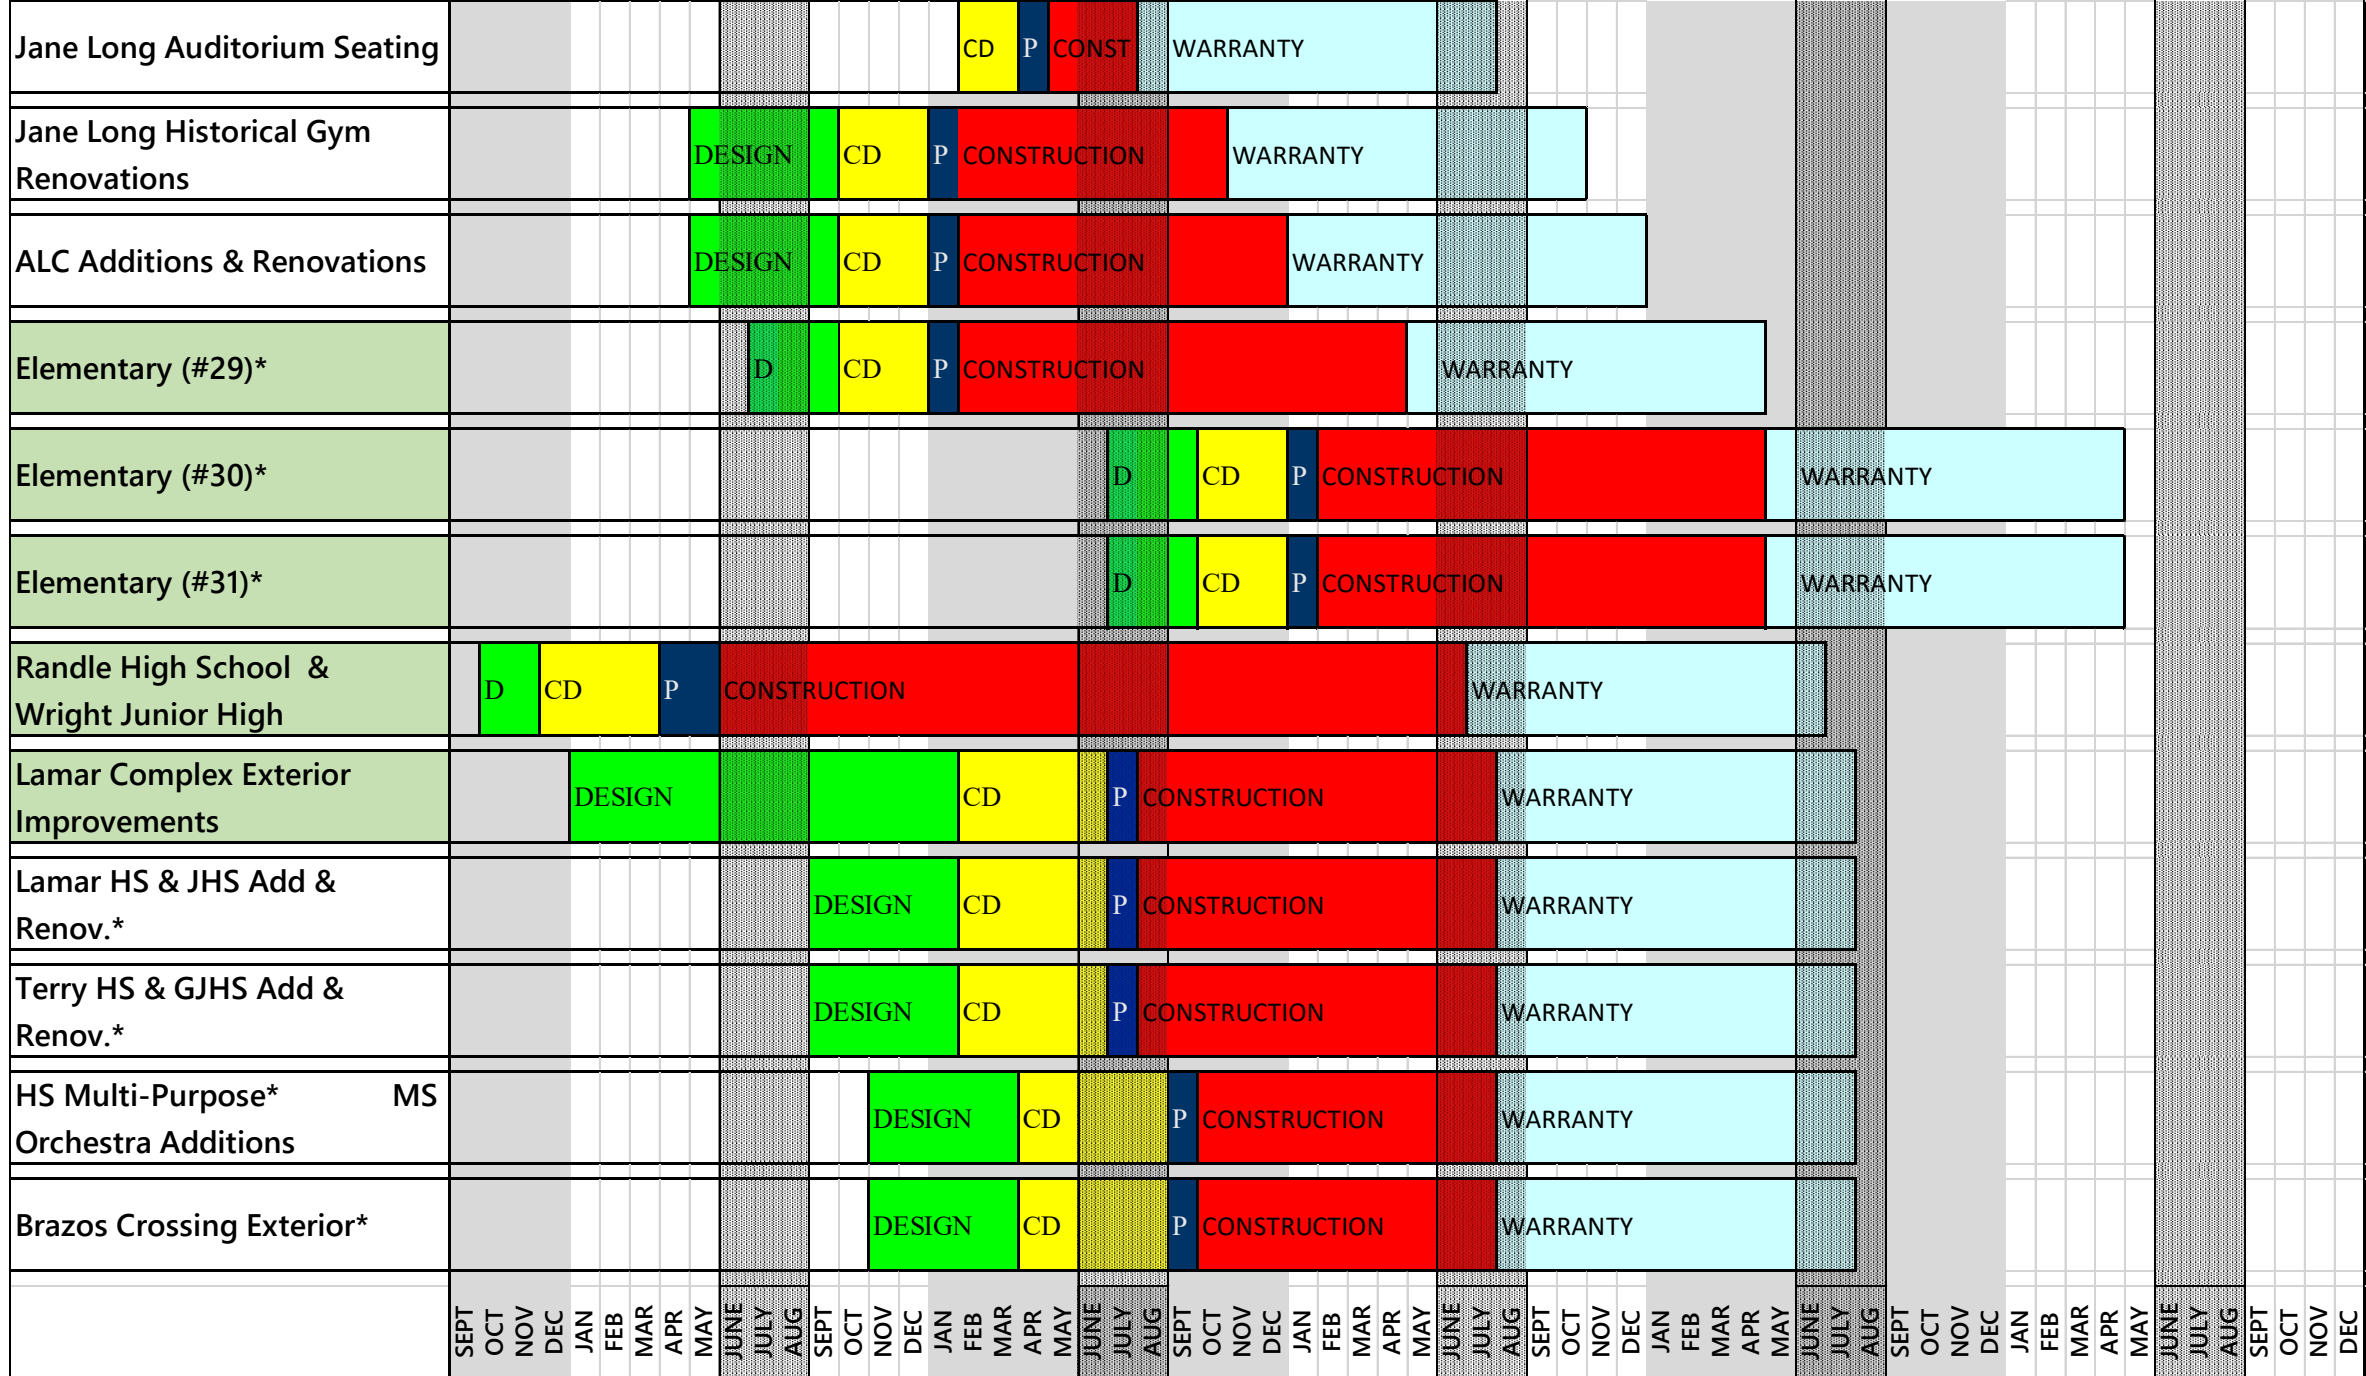

SEPT OCT NOV DEC JAN FEB MAR APR MAY JUNE JULY AUG
SEPT OCT NOV DEC JAN FEB MAR APR MAY JUNE JULY AUG
SEPT OCT NOV DEC JAN FEB MAR APR MAY JUNE JULY AUG
SEPT OCT NOV DEC JAN FEB MAR APR MAY JUNE JULY AUG
SEPT OCT NOV DEC JAN FEB MAR APR MAY JUNE JULY AUG
SEPT OCT NOV DEC JAN FEB MAR APR MAY JUNE JULY AUG

2018

2019

2020

2021

2022

2023
