



**Bond**

**★ 2017**

**LAMAR CONSOLIDATED ISD**

# Construction Manager Agent

- The CMA ranking was approved at the November Board Meeting
- Contract negotiations are ongoing.



# Austin Elementary & Seguin ECC Roof Replacement

- **Austin Elementary**
  - Complete
- **Seguin Early Childhood Center**
  - Removal of the old roof is 100% complete
  - Addition of new roof is 100% complete
  - Detail work is in progress
  - Project completion January 31, 2019



# Classroom Intruder Lockset Project

- Electrified hardware (door buzzers) have been activated. Some corrections are being addressed.
- Classroom Security Intruder Latchbolts installation are complete with exception of Travis Elementary and Austin Elementary.




# Child Nutrition Serving Lines

- Huckabee Architects are currently working on a design for the additional lines to be completed during summer of 2019.



# Facilities Assessment & Long Range Facilities Plan

- Facilities & Planning has conducted a kick off meeting with PBK Architects, Inc.
- Schedules are under development

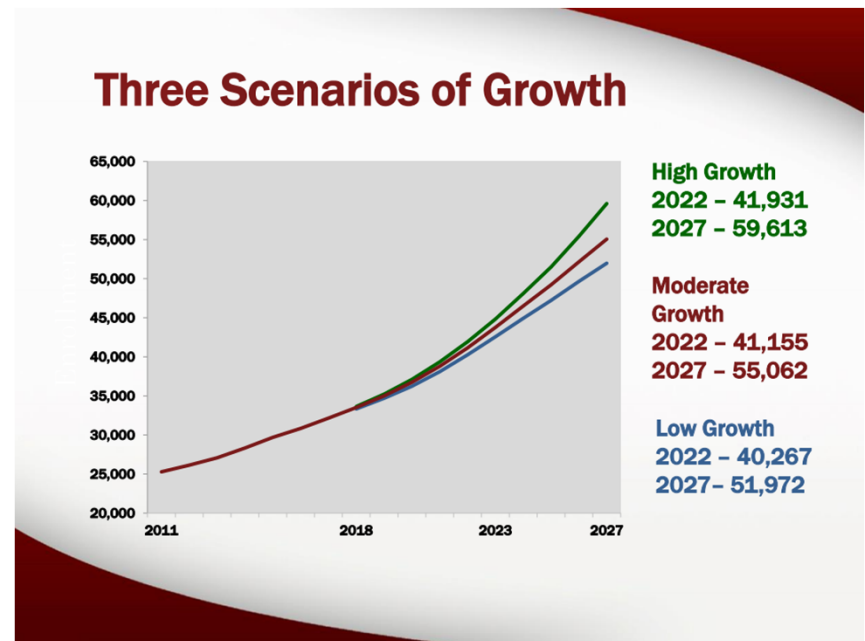

# High School #6 & Junior High School #6

- Recommendation for design development on the February Board Agenda
- Traffic Study has begun.
- 75% CDs due 1/24.
- Substantial Completion scheduled for May 7, 2021.




3D ENTRANCE PERSPECTIVE  
NEW LAMAR CONSOLIDATED HIGH SCHOOL 6 - OPTION 1

LAMAR CISD PRBK  
A PROUD TRADITION | A BRIGHT FUTURE

**Bond2017**  
LAMAR CONSOLIDATED ISD

# Synthetic Turf & Track Project

- Synthetic turf replacement at Foster, Fulshear, George Ranch, and Terry.
- Track replacements at Foster and Traylor Stadium.
- This project will be released for Competitive Sealed Proposals (CSP) in February.
- Contractor recommendation is scheduled for the March Board agenda.

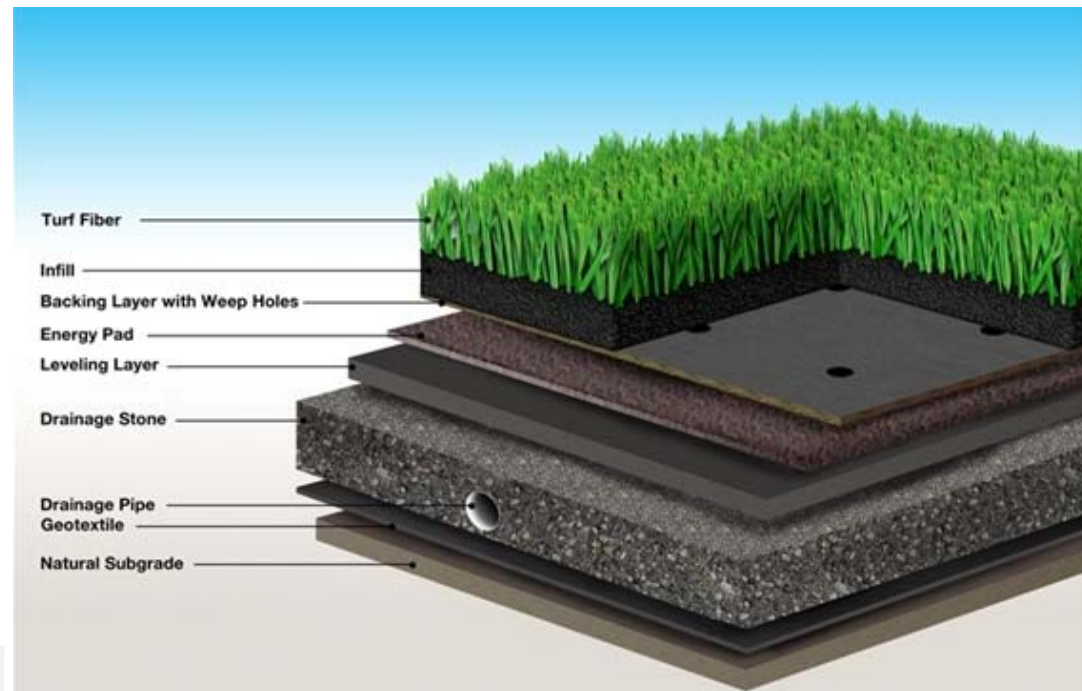



# Bond 2017 January Board Agenda Items

- CONSIDER APPROVAL OF MICRO INTEGRATION VIDEO SURVEILLANCE INTEGRATION SERVICES FOR THE NEW HIGH SCHOOL #6
- CONSIDER APPROVAL OF MICRO INTEGRATION VIDEO SURVEILLANCE INTEGRATION SERVICES FOR THE NEW JUNIOR HIGH SCHOOL #6



The logo features the word "Bond" in a dark blue, bold, sans-serif font, followed by "2017" in a larger, bold, yellow sans-serif font. A yellow five-pointed star is positioned to the left of the "B" in "Bond". Below "2017", the text "LAMAR CONSOLIDATED ISD" is written in a smaller, dark blue, all-caps sans-serif font. The entire logo is enclosed in a thin grey border.

# Bond 2017

LAMAR CONSOLIDATED ISD

## 2017 Bond Referendum summary

Project	Budget	Encumbered	Unencumbered
Austin Roof Replacement	\$1,900,000.00	\$854,317.00	\$1,045,683.00
Seguin Early Childhood Roof Replacement	\$1,900,000.00	\$983,211.00	\$916,789.00
Terry High Serving Line	\$650,000.00	\$201,586.32	\$448,413.68
George Junior High Serving Line	\$650,000.00	\$183,413.68	\$466,586.32
New High School #6	\$126,500,000.00	\$3,234,936.00	\$123,265,064.00
New Junior High #6	\$62,000,000.00	\$1,606,688.00	\$60,393,312.00
Technology	\$34,326,000.00	\$1,950,635.30	\$32,375,364.70

**LAMAR CISD 2017 BOND PROGRAM - PROJECT LIST**

1st SALE	2018				2019				2020				2021				2020				2021																			
PROJECTS	SEPT	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUNE	JULY	AUG	SEPT	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUNE	JULY	AUG	SEPT	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUNE	JULY	AUG	SEPT	OCT	NOV	DEC
Austin ES & Seguin ES Re-Roof	CONSTRUCTION				WARRANTY																																			
Terry & George Serving Lines	CONSTRUCTION				WARRANTY																																			
Classroom Intruder Locksets	CONSTRUCTION				WARRANTY																																			
High School 6 & Junior High 6	DESIGN				CD				BID				CONSTRUCTION				WARRANTY																							
High School Artificial Turf					CD				BID				CONSTRUCTION				WARRANTY																							
Foster HS Athletic Improvements					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
CES, WES, WMS, NWS Improv.					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
ES Cooler/Freezer Replacement					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
Fuel Tank Replacement*					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
Lamar Complex Improvements					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
High School LOTE Lab Renov.*					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
Jane Long Historical Gym Renov.*					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
Elementary (#29)					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
	SEPT	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUNE	JULY	AUG	SEPT	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUNE	JULY	AUG	SEPT	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUNE	JULY	AUG	SEPT	OCT	NOV	DEC
2nd SALE	2018				2019				2020				2021				2022				2023																			
PROJECTS	SEPT	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUNE	JULY	AUG	SEPT	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUNE	JULY	AUG	SEPT	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUNE	JULY	AUG	SEPT	OCT	NOV	DEC
New ALC Building*					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
Lamar HS & JHS Add & Renov.*					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
Bowie ES & Jackson ES Improv.*					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
FHS, BJHS, JES, PES, LES Improv.*					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
Exterior Improv. SES, TRES, FHS*					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
Seimans Controls Upgrade*					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
HS Multi-Purpose*					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
Brazos Crossing Exterior*					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
MS Orchestra Additons*					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
New Elementary 30 & 31*					DESIGN				CD				BID				CONSTRUCTION				WARRANTY																			
	SEPT	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUNE	JULY	AUG	SEPT	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUNE	JULY	AUG	SEPT	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUNE	JULY	AUG	SEPT	OCT	NOV	DEC
	2018				2019				2020				2021				2022				2023																			
