

# Gray Elementary

Opening August 2023

MEP Installation Ongoing

Installation of Window Frames

Mechanical Yard Progress Photo





# James E. Steenbergen Middle School

Opening August 2024

Construction Contract A101 Executed

Contractor has Mobilized and Began Earthworks







# Viola Randle Elementary School (33)

Opening August 2024

Construction Documents Issued for Proposals

Construction Manager At Risk Subcontractor Proposals Due November 17

Guaranteed Maximum Price (GMP) #1  
Recommendation on December Board Agenda

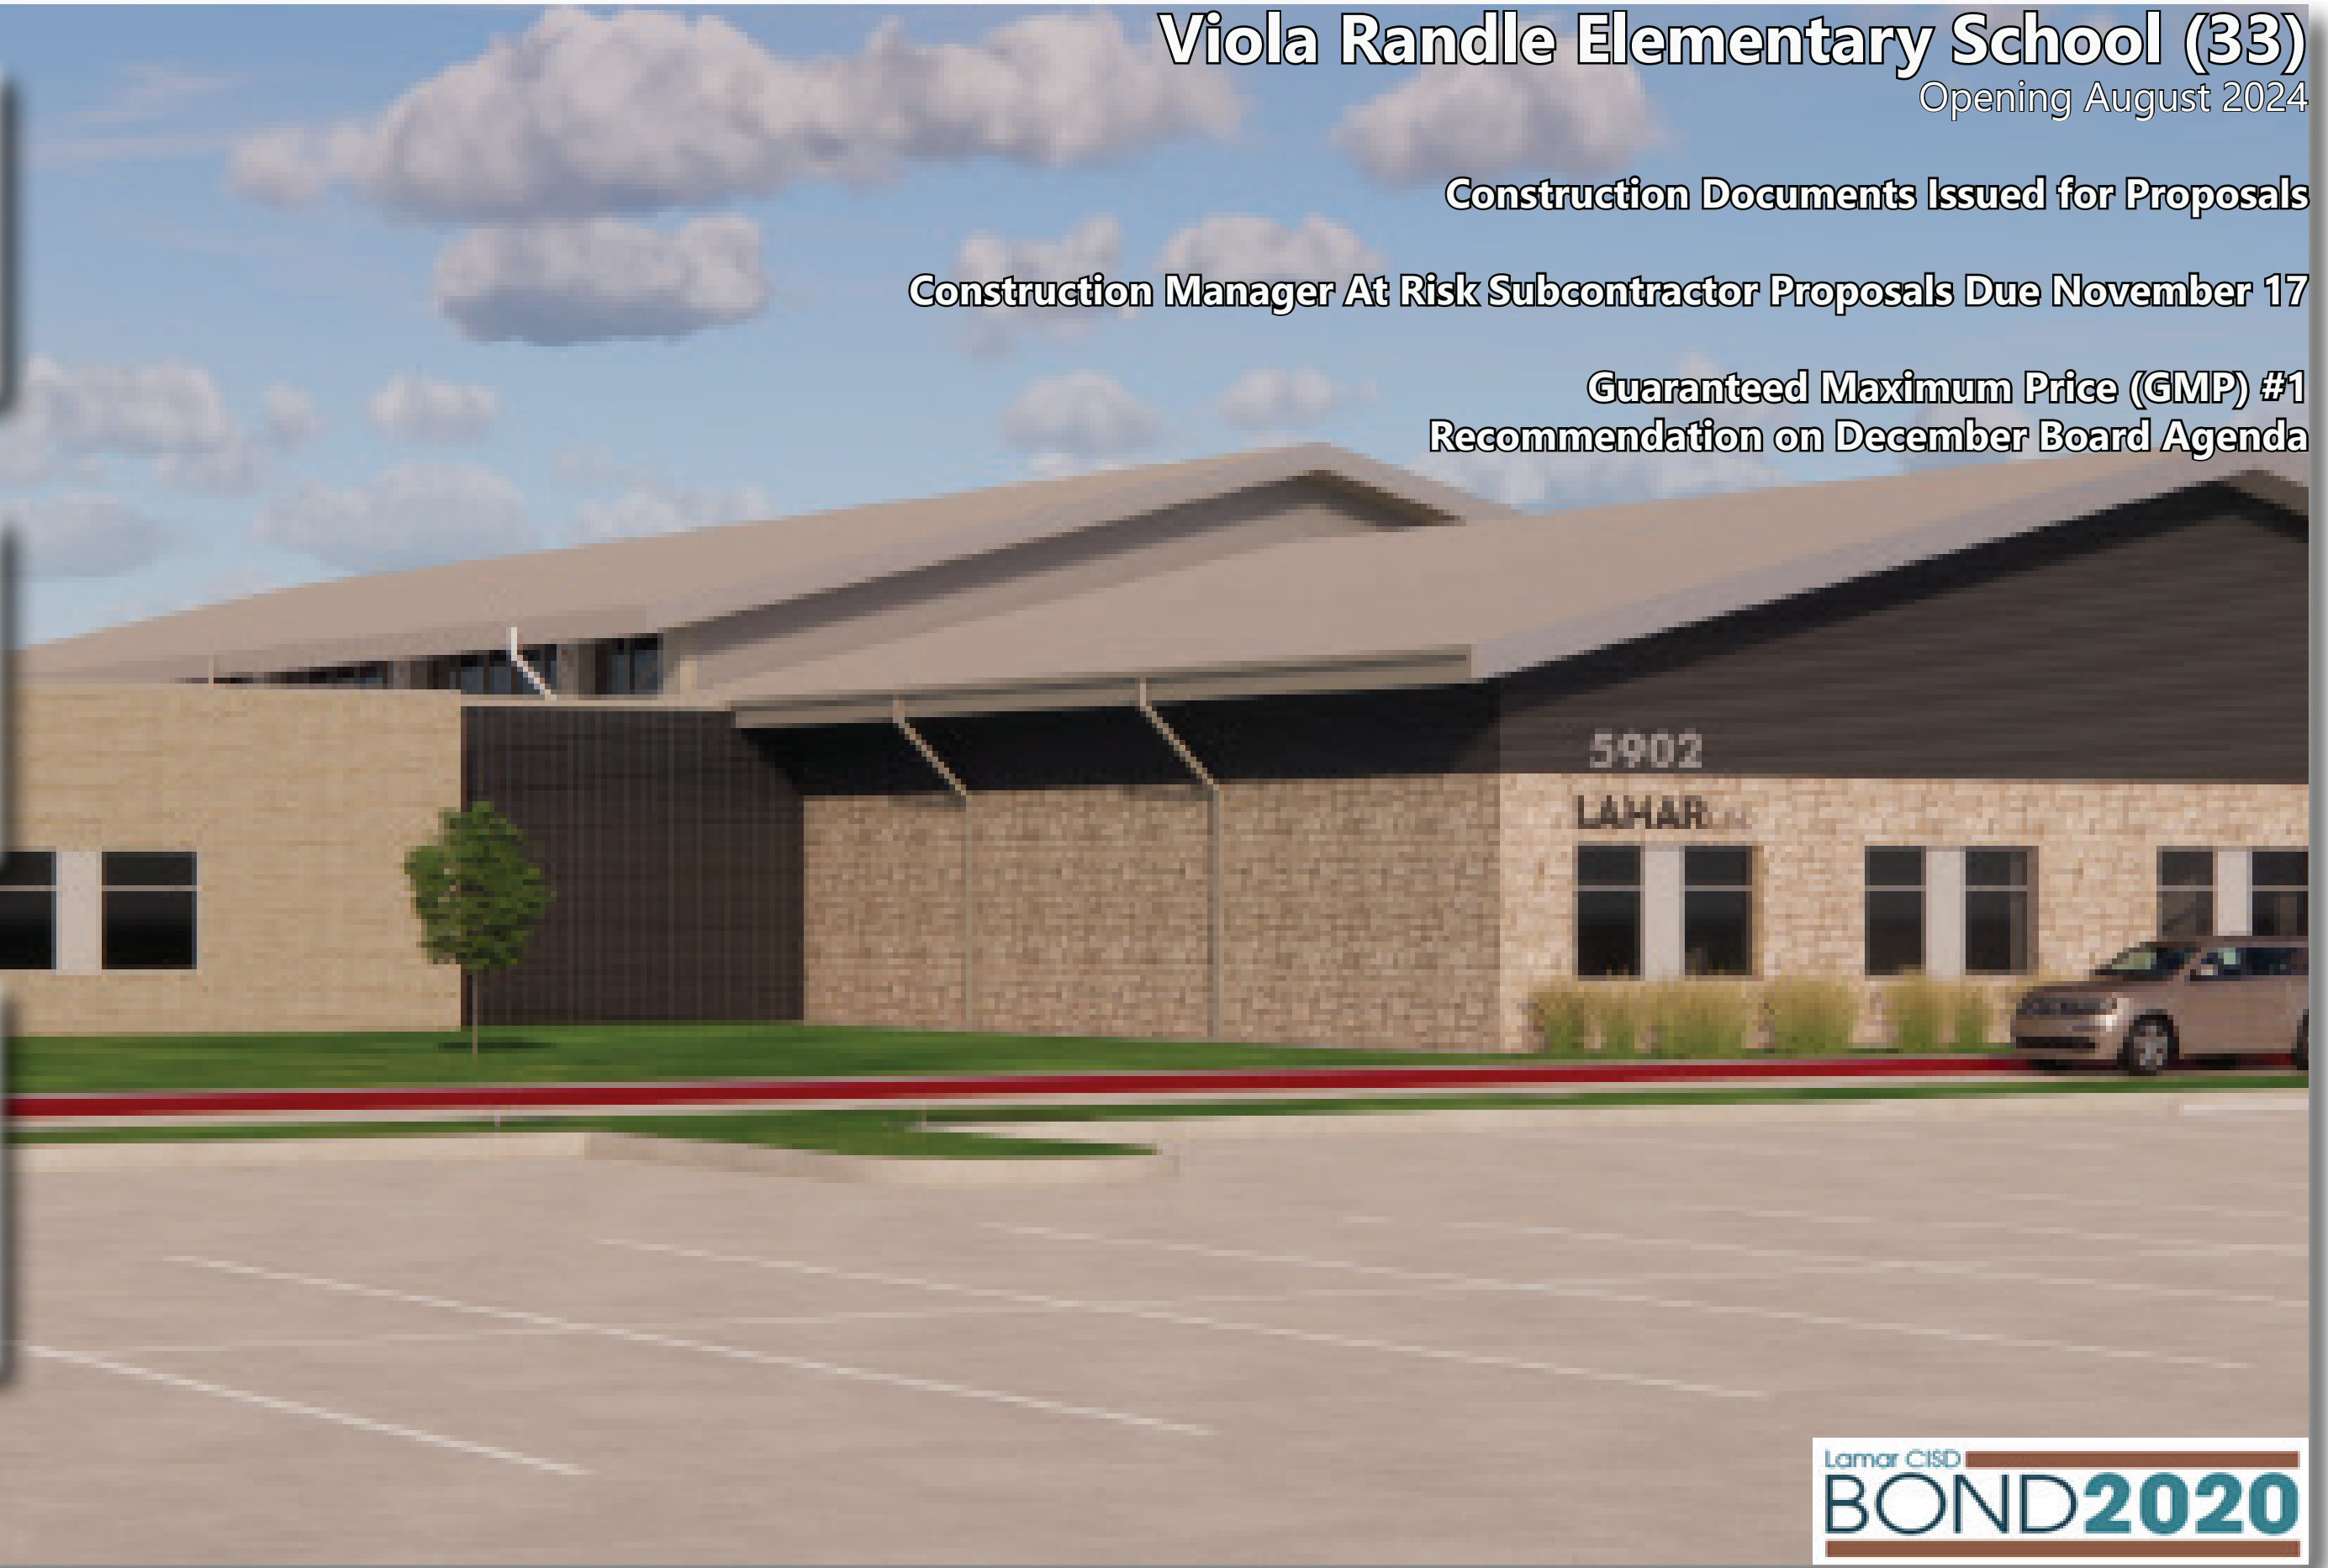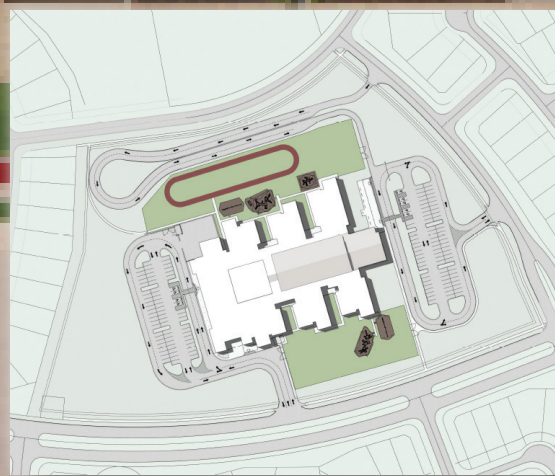



# Willie Melton Sr. Elementary School (34)

Opening August 2024


Construction Documents Issued for Proposals

Proposal Opening November 15

Contractor Recommendation on  
December Board Agenda



WILLIE MELTON SR. ELEMENT

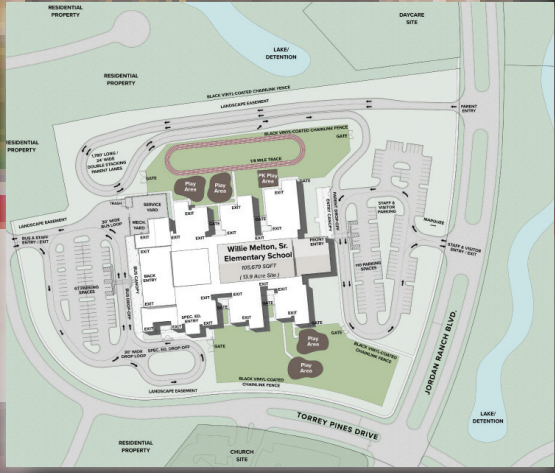



# Austin Elementary Additions & Renovations

Complete April 2023

Art Classroom – Storage Room Shelving  
Installed

Interior Restrooms – Installation of New  
Ceiling Tiles Completed

Front Vestibule – Door Frame for New  
Conference Room  
Installed





# Beasley Elementary Additions & Renovations

Complete February 2023

New Furniture Installed at Vestibule/ Reception  
Corridor

New Furniture Installed in Reception Area of  
New Building Addition

New Furniture Installed in Principal's Office





# Bowie Elementary Additions & Renovations

Complete January 2023

New Furniture Installed in Private Cot Room #2

New WAP Installed in New Building Addition

Gates Adjusted to Narrow Bottom Gap





# Campbell Elementary Re-Roof

Complete November 2022

Project Is Close To Substantial Completion





# Dickinson Elementary Re-Roof

Complete December 2022

Exterior Canopy is Complete

Contractor has Demobilized





# George Junior High Renovations

Complete January 2024

Top Ply Sheet Installed Over Commons and Library Spaces (Area 9)

Base Ply Sheet Installation Completed Over Kitchen Space (Area 11)

Top Ply Sheet Installed Over Science Lab Wing Spaces (Area 10)





# Huggins Elementary Additions & Renovations

Complete January 2023

Backing Plates Installed

Wallpaper Scope Completed

Dedication Plaque Reinstalled





# Jackson Elementary Additions & Renovations

Complete December 2022

Completed Roof

Principal's New Office Set Up

New Vinyl Supergraphics Being Installed





# Lamar Consolidated High School New Tennis Courts

Complete October 2022

Tennis Court Project Substantially Complete

Punch List Correction On-Going

Close-Out Documents in Process of Being Reviewed





# Williams Elementary New Parent Loop Drive Complete August 2022

