

Gray Elementary

Opening August 2023

MEP Installation Ongoing
Drywall Installation Ongoing
Roof Assembly Installation Ongoing



James E. Steenbergen Middle School

Opening August 2024

Construction Contract A101 Executed

Contractor Has Mobilized And Began Earthworks




Viola Randle Elementary School (33)

Opening August 2024

Construction Documents Issued for Proposals

Construction Manager at Risk Subcontractor Proposals Due November 17

Guaranteed Maximum Price (GMP) #1
Recommendation on December Board Agenda

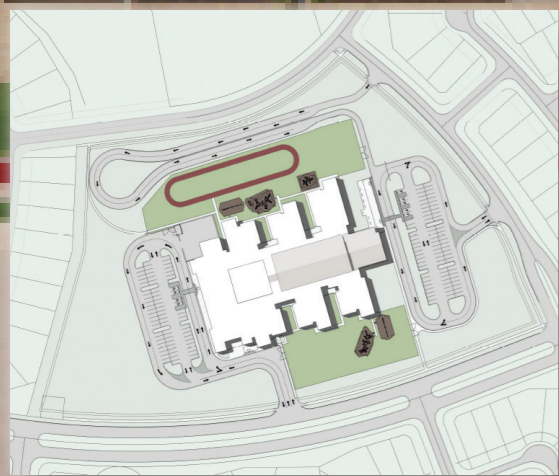

Willie Melton Sr. Elementary School (34)

Opening August 2024


Construction Documents Issued for Proposals

Proposal Opening November 15

Contractor Recommendation on December Board Agenda



WILLIE MELTON SR. ELEMENT

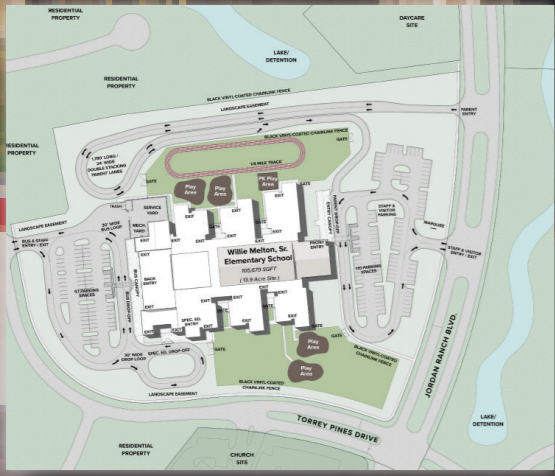

Austin Elementary Additions & Renovations

Complete April 2023

Vestibule - Ductwork Insulation Completed

Art Classroom - North Section Sidewalk
Poured

Art Classroom - VCT Completed



Beasley Elementary Additions & Renovations

Complete February 2023

Gypsum Board Ceiling Installed

Drywall Tape and Float Completed in New
Building Addition

Epoxy Resin Floor Finish in New Admin
Restroom



Bowie Elementary Additions & Renovations

Complete January 2023

Casework in Principal's Office Installed

Casework in Counselor's Office Installed

New Access Gate Installed



Campbell Elementary Re-Roof

Complete November 2022

Project Is Close to Substantial Completion



Dickinson Elementary Re-Roof

Complete December 2022

Finalizing Installation Standing
Roof/Ladders

Cap Sheet Application Complete

Roof Hatch/Safety Rail Installed



George Junior High Renovations

Complete January 2024

Area 10 Base Sheet Installed and Terminated at Roof Expansion Joint (Science Lab Wing)

Existing Gravel Spud Back and Vacuum Near Completion Over Second Half of Area 10 Roof

New Metal Roof Panel Installation Over Area 4 Raised Roof (Band Hall Space)



Huggins Elementary Additions & Renovations

Complete January 2023

Completed Stucco

Access Control Installed at Gate
Leading to Portables

Additional Interior Finishes Being Installed



Jackson Elementary Additions & Renovations

Complete December 2022

Temporary Fencing Removed - Sod Installed

New Furniture Delivered

New Security Cameras Installed



Lamar Consolidated High School New Tennis Courts

Complete October 2022

Tennis Court Project Substantially Complete

Punch List Correction On-Going

Close-Out Documents In Process of Being Reviewed



Williams Elementary New Parent Loop Drive Complete August 2022

