

Monthly Report May 2021

Dr. Thomas E. Randle High School & Harry Wright Junior High School

Koeblen Rd/FM 2977 traffic light will be active the week of 5/17.

Final interior finishes are in progress.

Substantial Completion is scheduled for 6/1.



Transportation Fuel Tank Replacement

Morris & Associates is the Firm of Record.

New system is fully operational.

Soil remediation testing is in progress.



Jane Long Historic Gym Renovations

VLK is the Architect of Record.

Interior finished and landscaping are in progress.

Substantial Completion is scheduled for 5/24.



ALC/1621 Additions and Renovations

VLK is the Architect of Record.

Masonry, MEP, and roofing are in progress.



Lamar CHS & Lamar JHS Additions & Renovations

PBK is the Architect of Record.

High School. Completing interior finishes in new classrooms.

Junior High. Choir/Orchestra interior finishes are in progress.

North Athletics Site. Masonry, roof, and MEP rough-in are in progress.

Traylor Stadium. Visitor locker room masonry, roof, and MEP are in progress.



Terry HS & George JHS Additions & Renovations

VLK Architects is the Architect of Record.

Terry. Band Hall renovations and Multi-Purpose Room masonry are in progress.

George Jr. Band Hall MEP and roof are in progress. Forum stage renovations are in progress.



Multi-Purpose Room (HS) & Orchestra (MS) Additions

PBK is the Architect of Record.

Multi-Purpose Rooms. Foster, Fulshear, and George Ranch construction is in progress.

Orchestra Rooms. Navarro, Ryon Wertheimer, and Wessendorff construction is in progress.



Brazos Crossing Exterior Improvement

VLK is the Architect of Record.

Final payment recommendation is scheduled for the June Board Meeting.



Fletcher Morgan, Jr. Elementary School

VLK is the Architect of Record.


Damp proofing, masonry, roof, and MEP rough-in are in progress.



Maxine Phelan Elementary School

VLK is the Architect of Record.

Permitting is in process.

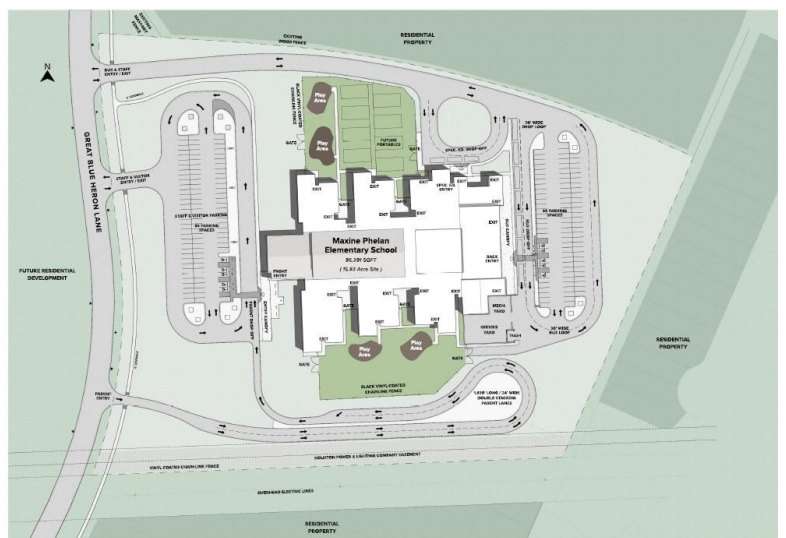

2017 BOND REFERENDUM SUMMARY					
PROJECT NAME	ORIGINAL BUDGET	BUDGET CHANGE	PROJECT BUDGET	COMMITTED	BALANCE
Roberts Middle School Orchestra Room	\$1,100,000.00	\$0.00	\$1,100,000.00	\$1,100,000.00	\$0.00
Austin ES Re-Roof	\$1,900,000.00	(\$529,504.00)	\$1,370,496.00	\$897,273.00	\$473,223.00
Seguin ECC Re-Roof	\$1,900,000.00	\$0.00	\$1,900,000.00	\$982,961.00	\$917,039.00
Terry HS Serving Lines	\$680,000.00	\$0.00	\$680,000.00	\$656,123.95	\$23,876.05
George JHS Serving Lines	\$620,000.00	\$0.00	\$620,000.00	\$528,728.39	\$91,271.61
Classroom Intruder Locks	\$400,000.00	\$0.00	\$400,000.00	\$390,985.72	\$9,014.28
High School LOTE Lab Renovations- <i>Lamar /Terry / Foster</i>	\$1,050,000.00	\$0.00	\$1,050,000.00	\$198,565.00	\$851,435.00
ES Cooler/Freezer Replacement - <i>Austin / Bealsley / Huggins / Pink / Seguin / Taylor Ray / Travis / Williams</i>	\$1,400,000.00	\$0.00	\$1,400,000.00	\$1,230,756.00	\$169,244.00
Summer 2019 Multi-Campus Improv. - <i>Campbell ES Carpet / Campbell ES VWC / Navarro MS Carpet / Navarro MS Intercom / Wessendorff MS Carpet / Wessendorff MS VWC / Williams ES Carpet / Williams Admin. Renov. / Williams ES Fire Sprinklers</i>	\$2,740,000.00	\$114,000.00	\$2,854,000.00	\$2,824,511.64	\$29,488.36
HS Field Turf & Foster HS Track - <i>GR Turf / Fulshear Turf / Foster Turf / Terry Turf / Foster Track</i>	\$9,082,719.00	\$0.00	\$9,082,719.00	\$7,352,923.72	\$1,729,795.28
Foster HS Athletic Improvements- <i>HS Baseball & Softball Improv. / HS Field House Locker Replacement</i>	\$867,281.00	\$0.00	\$867,281.00	\$829,768.00	\$37,513.00
Dr. Thomas E. Randle High School- <i>High School / Turf / Multi-Purpose Room</i>	\$127,630,000.00	\$0.00	\$127,630,000.00	\$115,386,733.73	\$12,243,266.27
Harry Wright Junior High School	\$62,000,000.00	\$0.00	\$62,000,000.00	\$55,441,207.82	\$6,558,792.18
Lamar CHS & Lamar JHS Exterior Improvements - <i>Traylor Visitor Locker Room / Sub-Varsity Field / HS Multi-Purpose Room Add/ Turf/ Improved Drainage, Parking & Sidewalks / Revised JHS Drop Off / JHS HVAC Upgrades</i>	\$15,340,000.00	\$0.00	\$15,340,000.00	\$2,987,206.00	\$12,352,794.00
Lamar CHS & Lamar JHS Additions & Renovations - <i>HS Admin Renov. / LGI Add / HS Expand Band Hall / JHS Choir Add / JHS Intercom Upgrade</i>	\$8,480,000.00	\$0.00	\$8,480,000.00	\$2,278,678.00	\$6,201,322.00
Terry HS & George JHS Additions & Renovations- <i>JHS Renovated Locker Room / JHS Band Add / JHS Visitor Parking Add / JHS Forum Renov. / HS replace Wood Football Bleacher / HS Exterior Door & Window Replacement / HS Band & Chior Add / HS Resurface Parking / HS Multi-Purpose Room</i>	\$14,650,000.00	\$0.00	\$14,650,000.00	\$8,154,309.00	\$6,495,691.00
Traylor Stadium Press Box Replacement	\$2,800,000.00	\$1,632,000.00	\$4,432,000.00	\$4,343,843.00	\$88,157.00
New Alternative Learning Center	\$12,200,000.00	\$0.00	\$12,200,000.00	\$1,228,860.00	\$10,971,140.00
Jane Long ES Historical Gym Renovations	\$3,200,000.00	\$0.00	\$3,200,000.00	\$3,048,979.00	\$151,021.00
Jane Long Auditorium Seating	\$125,000.00	\$0.00	\$125,000.00	\$0.00	\$125,000.00
Transportation - Replace Underground Fuel Tank	\$900,000.00	\$415,504.00	\$1,315,504.00	\$1,308,014.00	\$7,490.00
HS Multi-Purpose Rooms & MS Orchestra Adds - <i>Foster MP / GR MP / Fushear MP / Narvarro Orch / Wessendorff Orch / Ryon Orch / Wertheimer Orch / Foster HS Add Parking</i>	\$9,570,000.00	\$0.00	\$9,570,000.00	\$9,119,829.30	\$450,170.70
Multi-Campus Carpet Replacement - <i>Foster HS / Briscoe JHS / Jackson ES / Pink ES / Long ES</i>	\$2,310,000.00	\$0.00	\$2,310,000.00	\$2,168,225.00	\$141,775.00
Summer 2020 Multi-Campus ES Renovations - <i>Austin Office Renov. / Bowie Add 25 Parking Spaces / Bowie Replace Entry Canopy / Bowie Serving Line Renov. / Bowie Enlarge Cafeteria / Jackson Drainage Improv. / Jackson Serving Line Renov. / Smith Renov. Courtyard / Ray Improv Drainage in Parking Lot / Controls Upgrade</i>	\$3,370,000.00	\$0.00	\$3,370,000.00	\$3,155,402.00	\$214,598.00
Brazos Crossing Renovations	\$1,800,000.00	\$0.00	\$1,800,000.00	\$115,420.00	\$1,684,580.00
Morgan Elementary School	\$30,200,000.00	\$0.00	\$30,200,000.00	\$24,487,855.00	\$5,712,145.00
Maxine Phelan Elementary School	\$32,600,000.00	\$0.00	\$32,600,000.00	\$12,975.00	\$32,587,025.00
New Elementary School #31	\$35,200,000.00	\$0.00	\$35,200,000.00	\$0.00	\$35,200,000.00
Land	\$20,000,000.00	\$0.00	\$20,000,000.00	\$0.00	\$20,000,000.00
TOTAL	\$404,115,000.00	\$1,632,000.00	\$405,747,000.00	\$250,230,133.27	\$155,516,866.73
TOTAL FACILITY & PLANNING BOND	\$404,115,000.00	funded by 2014			
REMAINING FACILITY & PLANNING BOND	\$155,516,866.73	bond available funds			

Denotes completed projects

2017 BOND TECHNOLOGY SUMMARY					
PROJECT NAME	ORIGINAL BUDGET	BUDGET CHANGE	PROJECT BUDGET	COMMITTED	BALANCE
IFP-Interactive Flat Panel	\$9,044,000.00	\$0.00	\$9,044,000.00	\$9,015,570.00	\$28,430.00
PTO-Printer Refresh	\$1,440,000.00	\$0.00	\$1,440,000.00	\$1,347,360.00	\$92,640.00
CCU-Campus Core Uplink	\$740,000.00	\$0.00	\$740,000.00	\$737,926.00	\$2,074.00
ES0-Expanded Storage	\$400,000.00	\$0.00	\$400,000.00	\$400,000.00	\$0.00
SC0-Security Cameras	\$250,000.00	\$0.00	\$250,000.00	\$250,000.00	\$0.00
TEL-Telephones	\$890,000.00	\$0.00	\$890,000.00	\$747,672.00	\$142,328.00
CRO-Computer Refresh	\$18,344,000.00	\$0.00	\$18,344,000.00	\$18,324,094.00	\$19,906.00
LC0-Laptop Carts	\$450,000.00	\$0.00	\$450,000.00	\$0.00	\$450,000.00
SCN-Eduphoria Scanners	\$122,000.00	\$0.00	\$122,000.00	\$121,450.00	\$550.00
IA0-Interact	\$2,646,000.00	\$0.00	\$2,646,000.00	\$0.00	\$2,646,000.00
TOTAL	\$34,326,000.00	\$0.00	\$34,326,000.00	\$30,944,072.00	\$3,381,928.00
TOTAL TECHNOLOGY BOND	\$34,326,000.00				
REMAINING TECHNOLOGY BOND	\$3,381,928.00				

2017 BOND TRANSPORTATION SUMMARY					
PROJECT NAME	ORIGINAL BUDGET	BUDGET CHANGE	PROJECT BUDGET	COMMITTED	BALANCE
New Bus Purchase	\$5,175,000.00	(\$7,300.00)	\$5,167,700.00	\$2,560,746.00	\$2,606,954.00
Add Air to Buses	\$1,335,000.00	\$0.00	\$1,335,000.00	\$0.00	\$1,335,000.00
Smart Tag	\$500,000.00	\$7,300.00	\$507,300.00	\$507,250.91	\$49.09
TOTAL	\$7,010,000.00	\$0.00	\$7,010,000.00	\$3,067,996.91	\$3,942,003.09
TOTAL TRANSPORTATION BOND	\$7,010,000.00				
REMAINING TRANSPORTATION BOND	\$3,942,003.09				

